

CONSTRUCTION UPDATE

NEW NORTH OLMSTED PK-5 SCHOOL AND RELATED PROJECTS



April 2025



Main Entrance



Primary Entrance



Kindergarten ELA



EXPERIENCED • DEPENDABLE • RESOURCEFUL

5802 Akron-Cleveland Road, Hudson, Ohio 44236 • (330) 656-9353





TABLE OF CONTENTS

3	EXECUTIVE SUMMARY
4-8	PROJECT SUMMARY / PHOTOS
9	COST SUMMARY
10-12	CONTINGENCY RECONCILIATION
13-14	CONSTRUCTION SCHEDULE



EXECUTIVE SUMMARY

Construction progress across all units is advancing steadily. In Unit A, CMU bearing walls, structural steel, and precast plank installations are ongoing, with stair towers, AHU installation, and slab on grade now completed. Upcoming work includes continuation of current activities and pouring the precast topping. Unit B mirrors similar progress, with CMU walls and structural steel in progress, precast plank and stair towers completed, and upcoming focus on continuation of CMU and steel work along with precast topping. Unit C kitchen slab on grade is poured, while gym CMU walls continue. In Unit D, below-grade CMU and stoning for slab on grade are underway, with preparations for slab on grade to follow. Lastly, Unit E is progressing with below-grade CMU and underground electrical installations, both of which will continue in the coming period. Overall, the project remains on track with key structural elements advancing in parallel across all units.

PROJECT SUMMARY



Unit A

April 2025 Progress

- CMU Bearing Walls– In Progress
- Structural Steel Installation– In Progress
- Pour Slab on Grade– Complete
- Set Precast Planks– In Progress
- Stair Towers– Complete
- Air Handler Unit Installation– Complete

Upcoming Progress

- CMU Bearing Walls
- Structural Steel Installation
- Set Precast Planks
- Pour Precast Topping

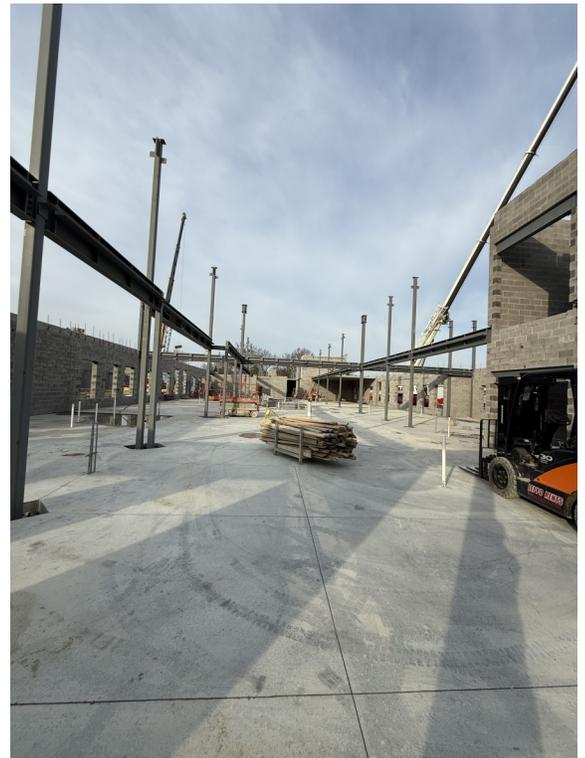

Structural Steel and Bearing Walls



Precast Plank Installation



Air Handler Units

PROJECT SUMMARY


Unit B

April 2025 Progress

- CMU Bearing Walls– In Progress
- Structural Steel Installation– In Progress
- Pour Slab on Grade– Complete
- Set Precast Planks– Complete
- Stair Towers– Complete

Upcoming Progress

- CMU Bearing Walls
- Structural Steel Installation
- Pour Precast Topping



Slab on Grade



Precast Planks

PROJECT SUMMARY


Unit C

April 2025 Progress

- CMU Bearing Walls– In Progress
- Pour Kitchen Slab on Grade– Complete

Upcoming Progress

- CMU Bearing Walls



Kitchen Slab on Grade




Gym Walls

PROJECT SUMMARY

Unit D

April 2025 Progress

- Below Grade CMU– In Progress
- Stoning for Slab on Grade– In Progress



Upcoming Progress

- Below Grade CMU
- Prep for Slab on Grade



Unit D North Side

PROJECT SUMMARY


Unit E

April 2025 Progress

- Below Grade CMU– In Progress
- Underground Electrical– In Progress

Upcoming Progress

- Below Grade CMU
- Underground Electrical



Unit E East Side

