


CONSTRUCTION UPDATE

NEW NORTH OLMSTED PK-5 SCHOOL AND RELATED PROJECTS



February 2025

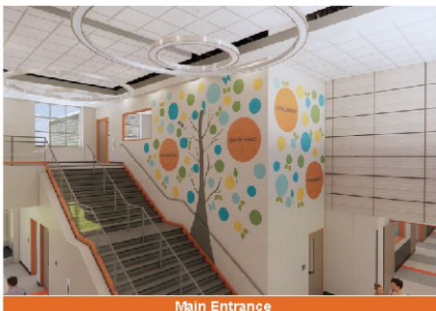

Main Entrance



Primary Entrance



Kindergarten ELA



EXPERIENCED • DEPENDABLE • RESOURCEFUL

5802 Akron-Cleveland Road, Hudson, Ohio 44236 • (330) 656-9353





TABLE OF CONTENTS

3	EXECUTIVE SUMMARY
4-8	PROJECT SUMMARY / PHOTOS
9	COST SUMMARY
10-12	CONTINGENCY RECONCILIATION
13-14	CONSTRUCTION SCHEDULE



EXECUTIVE SUMMARY

The project has experienced some weather delays, but work continues across all units. In Unit A, CMU bearing walls and stairwell walls are in progress, with work set to continue along with an upcoming slab-on-grade pour. Unit B has seen progress on CMU bearing walls, with ongoing work in this area and preparation for the slab-on-grade pour. Unit C foundations, below-grade CMU, and underground utilities are in progress, with work in these areas continuing. Unit D has progressed through foundations and underground plumbing, with upcoming work on below-grade CMU, underground utilities, and stoning for the slab-on-grade. Unit E has advanced with foundations and underground plumbing, with continued work in these areas as well as the installation of below-grade CMU.



North Olmsted PK-5

PROJECT SUMMARY

Site Development

February 2025 Progress

- Underground Site Electric– In Progress
- Light Pole Bases– In Progress
- Temp Power– Complete
- Permanent Power Preparation– In Progress



Upcoming Progress

- Natural Gas Piping
- Light Pole Bases
- Underground Site Electric
- Permanent Power Preparation

PROJECT SUMMARY


Unit A

February 2025 Progress

- CMU Bearing Walls– In Progress
- Stair Core– In Progress

Upcoming Progress

- CMU Bearing Walls
- Stair Core
- Pour Slab on Grade



Unit A West Side

PROJECT SUMMARY


Unit B

February 2025 Progress

- CMU Bearing Walls– In Progress

Upcoming Progress

- CMU Bearing Walls
- Pour Slab on Grade



Unit B South Bearing Wall and Stairwell

PROJECT SUMMARY


Unit C

February 2025 Progress

- Foundations– In Progress
- Below Grade CMU– In Progress
- Underground Plumbing– In Progress
- Underground Electrical– In Progress

Upcoming Progress

- Foundations
- Underground Plumbing
- Underground Electrical
- Below Grade CMU



Unit C Gym Below Grade CMU North Side



Unit C Underground Plumbing Main Corridor

PROJECT SUMMARY


Unit D

February 2025 Progress

- Foundations– Complete
- Underground Plumbing– In Progress

Upcoming Progress

- Below Grade CMU
- Underground Plumbing
- Underground Electrical
- Stoning for Slab on Grade

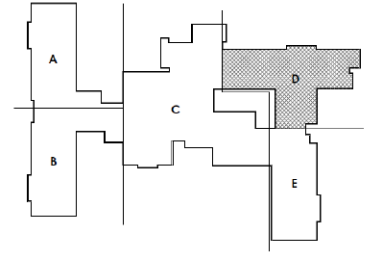

Unit D East Side

PROJECT SUMMARY


Unit E

February 2025 Progress

- Foundations– In Progress
- Underground Plumbing– In Progress

Upcoming Progress

- Foundations
- Underground Plumbing
- Underground Electrical
- Below Grade CMU



Unit E Underground Plumbing West Side

