


CONSTRUCTION UPDATE

NEW NORTH OLMSTED PK-5 SCHOOL AND RELATED PROJECTS




November 2024

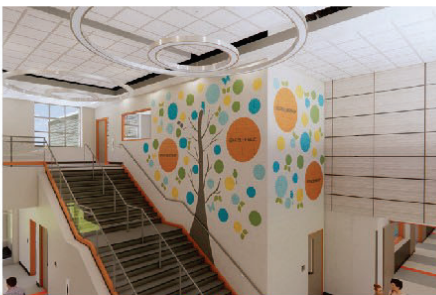

Main Entrance



Primary Entrance

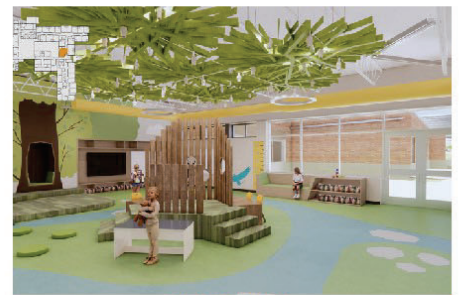

Kindergarten ELA



EXPERIENCED • DEPENDABLE • RESOURCEFUL

5802 Akron-Cleveland Road, Hudson, Ohio 44236 • (330) 656-9353





TABLE OF CONTENTS

3	EXECUTIVE SUMMARY
4-7	PROJECT SUMMARY / PHOTOS
8	COST SUMMARY
9-11	CONTINGENCY RECONCILIATION
12-13	CONSTRUCTION SCHEDULE



EXECUTIVE SUMMARY

Significant progress has been made across the project. In Site Development, work continued on underground site electric, waterline piping, and light pole bases, with upcoming efforts focused on natural gas piping, temporary power, permanent power preparation, and continuing light pole bases and underground electric. For Unit A, the foundations are complete, and work on underground plumbing is underway, with the next phase continuing underground plumbing and starting below grade CMU and underground electrical. In Unit B, foundations, below grade CMU, underground plumbing, and underground electrical are advancing, with upcoming activities extending these tasks and beginning slab on grade preparation. In Unit C, progress on foundations is in progress, with the next steps including underground plumbing, underground electrical, and below grade CMU. Overall, work is progressing as planned, with ongoing efforts laying the groundwork for the next stages of construction.

PROJECT SUMMARY

Site Development

November 2024 Progress

- Underground Site Electric– In Progress
- Waterline Piping– In Progress
- Light Pole Bases– In Progress



Upcoming Progress

- Natural Gas Piping
- Temp Power
- Permanent Power Preparation
- Light Pole Bases
- Waterline Piping
- Underground Site Electric



Waterline Piping East Side



Light Pole Base West Side

PROJECT SUMMARY


Unit A

November 2024 Progress

- Foundations– Complete
- Underground Plumbing– In Progress

Upcoming Progress

- Below Grade CMU
- Underground Electrical
- Underground Plumbing



Underground Plumbing Main Corridor



Unit A Foundations East Side

PROJECT SUMMARY


Unit B

November 2024 Progress

- Foundations– In Progress
- Below Grade CMU– In Progress
- Underground Plumbing– In Progress
- Underground Electrical– In Progress

Upcoming Progress

- Foundations
- Below Grade CMU
- Underground Plumbing
- Underground Electrical
- Slab-on-Grade Preparation



Underground Plumbing and Electrical



Unit B Below Grade CMU

PROJECT SUMMARY


Unit C

November 2024 Progress

- Foundations– In Progress

Upcoming Progress

- Underground Plumbing
- Underground Electrical
- Below Grade CMU



Unit C Gym Foundations West Side

