

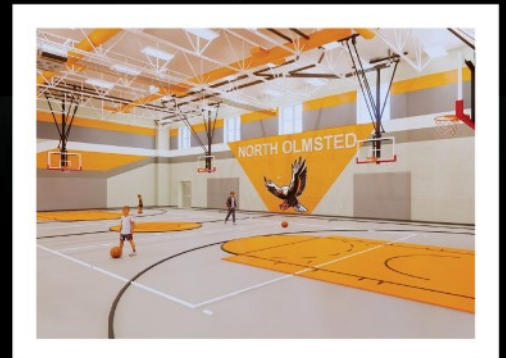


# CONSTRUCTION UPDATE

## NEW NORTH OLMSTED PK-5 SCHOOL AND RELATED PROJECTS

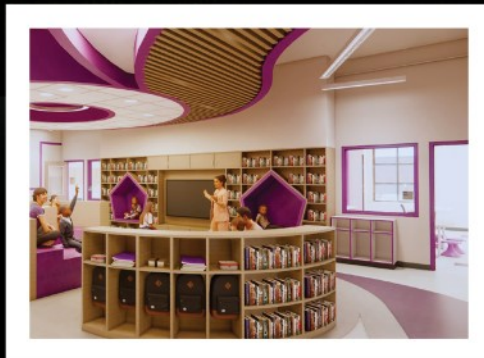

OCTOBER 2024

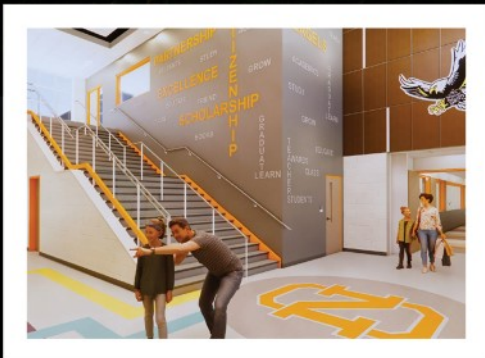

EXPERIENCED • DEPENDABLE • RESOURCEFUL

5802 Akron-Cleveland Road, Hudson, Ohio 44236 • (330) 656-9353





## North Olmsted PK-5

### EXECUTIVE SUMMARY

Progress on the project is advancing steadily. The building pad, site storm drainage, cement stabilization, asphalt binder, and Lorain Road utility concrete are all complete. Ongoing work includes light pole base installations, waterline piping, and underground site electrical. Upcoming progress will focus on installing natural gas piping, continuing underground site electrical work and pole bases, temporary power service, and advancing preparations for permanent power service. In Unit B, foundation work is in progress, with upcoming activities including below-grade CMU, underground plumbing and electrical, and preparation for the slab-on-grade. The project is proceeding as planned, with teams working diligently to maintain smooth progress throughout the project.



## PROJECT SUMMARY

### Site Development

#### October 2024 Progress

- Building Pad— Complete
- Site Storm Drainage— Complete
- Underground Site Electric— In Progress
- Cement Stabilization— Complete
- Asphalt Binder— Complete
- Waterline Piping— In Progress
- Light Pole Bases— In Progress
- Lorain Road Concrete— Complete

#### Upcoming Progress

- Natural Gas Piping
- Temp Power
- Permanent Power Preparation
- Light Pole Bases
- Underground Site Electric



*Domestic Water Piping to the Building*




*Main Electrical Service Duct Bank*

## PROJECT SUMMARY

### Unit B

#### October 2024 Progress

- Foundations— In Progress

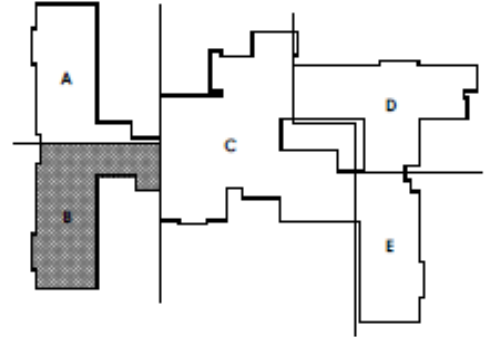

#### Upcoming Progress

- Below Grade CMU
- Underground Plumbing
- Underground Electrical
- Slab-on-Grade Preparation



*Unit B Column Pads*



*Unit B Foundations*
